

Appendix H



tear out aids

CONCRETE PRE-PLACEMENT CHECKLIST

The following checklist is supplied by Arxx Building Products to assist the Arxx installer prior to placing concrete in the Arxx™ Wallssystem. Arxx Building Products encourages the installer to exercise its use on each Arxx installation.

DATE: _____ **FOREMAN:** _____ **JOB:** _____

- Has all form support been installed?
- Were elevation changes properly handled?
- Are walls according to layout?
- Is alignment/scaffold system installed properly?
- Are scaffold planks secured?
- Are all openings installed?
- Has reinforcing been placed around all openings?
- Have anchor bolts or nails been provided for buck anchorage?
- Have bucks been secured to the wall?
- Are all service penetrations installed?
- Has the top course of forms been secured to the course below?
- Have all corner forms been secured?
- Have adjustable forms been taped?
- Have beam pockets been provided?
- Has floor system anchorage been installed?
- Is reinforcing in place as specified?
- Is wall straight?
- Has top course been protected from sockets filling with concrete?
- Is tool available for consolidation on site? (internal vibrator)
- Are strapping and screw gun available in case of a blowout?
- Has proper strength concrete been ordered per code or engineer?
- If placing direct from chute, is there room for truck to maneuver?

This listing is not meant to cover all aspects of review that an Installer might complete to have a successful Arxx Wallssystem installation. Because Arxx Building Products has no control over installation, workmanship, accessory materials, or conditions or application, no responsibility or expressed warranty, either as to merchantability or fitness for the particular purpose, is made as to the performance or results of an installation using Arxx Wallsystems.

CONCRETE POST-PLACEMENT CHECKLIST

The following checklist is supplied by Arxx Building Products to assist the Arxx™ installer to complete a number of post-placement checks and procedures prior to leaving the project jobsite. Arxx Building Products encourages the installer to exercise its use on each Arxx installation.

DATE:

FOREMAN:

JOB:

- Is wall straight?
- Has concrete been properly consolidated?
- Have all “tight” areas such as joist/beam pockets been consolidated?
- Has wall been checked for level?
- Has wall been troweled off as per plan?
- Have anchor bolts been placed?
- Is top of forms clean for continuation of Arxx forms?
- Has concrete been cleaned from alignment/scaffold system?
- Has concrete been cleaned off slab/footing?
- Have tools been cleaned?
- Have walls been re-checked for straight and level?

This listing is not meant to cover all aspects of review that an installer might complete to have a successful Arxx Wallsystem installation. Because Arxx Building Products has no control over installation, workmanship, accessory materials or conditions, or application, no responsibility or expressed warranty, either as to merchantability or fitness for the particular purpose, is made as to the performance or results of an installation using Arxx Wallsystem.


Corner Furring Tab Marking Template

Instructions for Use

Use template for locating and marking corner furring tabs on forms where tab location lines may not be visible.

1. Punch out location areas as indicated.
2. Fold template along fold line.
3. Placing on form with fold line at corner and aligning either of the lines with the top edge of the form.
4. With a marker or dabber, mark the screw mounting target locations. Screws can be applied anywhere indicated within the box outline.

Align to top
edge of form

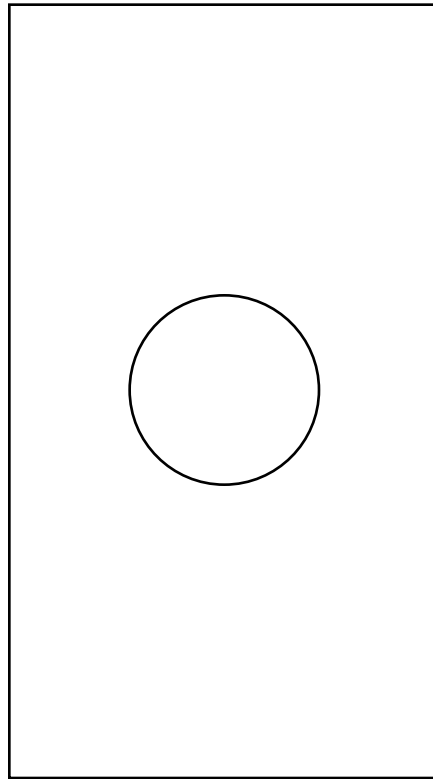

Fold line



Align to top
edge of form

